

AIP CANADA SUPPLEMENT 074/2026**AERODROME CONSTRUCTION – ÎLES-DE-LA-MADELEINE, QC (CYGR)**

**IMPORTANT: This AIP SUP is for situational awareness only.
NOTAMs are published in conjunction and take precedence**

Introduction and Validity

Rehabilitation of Runway 16-34 and replacement of electronic visual aids in the movement area are scheduled to take place at the Îles-de-la-Madeleine (YGR) Airport in 2026 and 2027.

Total Planned Duration: From 2026 to 2027.

Planned number of phases: 2

Phases completed: **0** of **2**

This AIP Supplement describes phase 1 only.

This AIP Supplement is expected to be replaced by 26 October 2026.

Legend

	Application/Symbol	Colour
Closed		Red
Runway Available for Taxi Only		Amber
Construction Activity Area		Grey

Phase 1A**Planned Construction Period**

- From 31 August 2026 to 26 October 2026

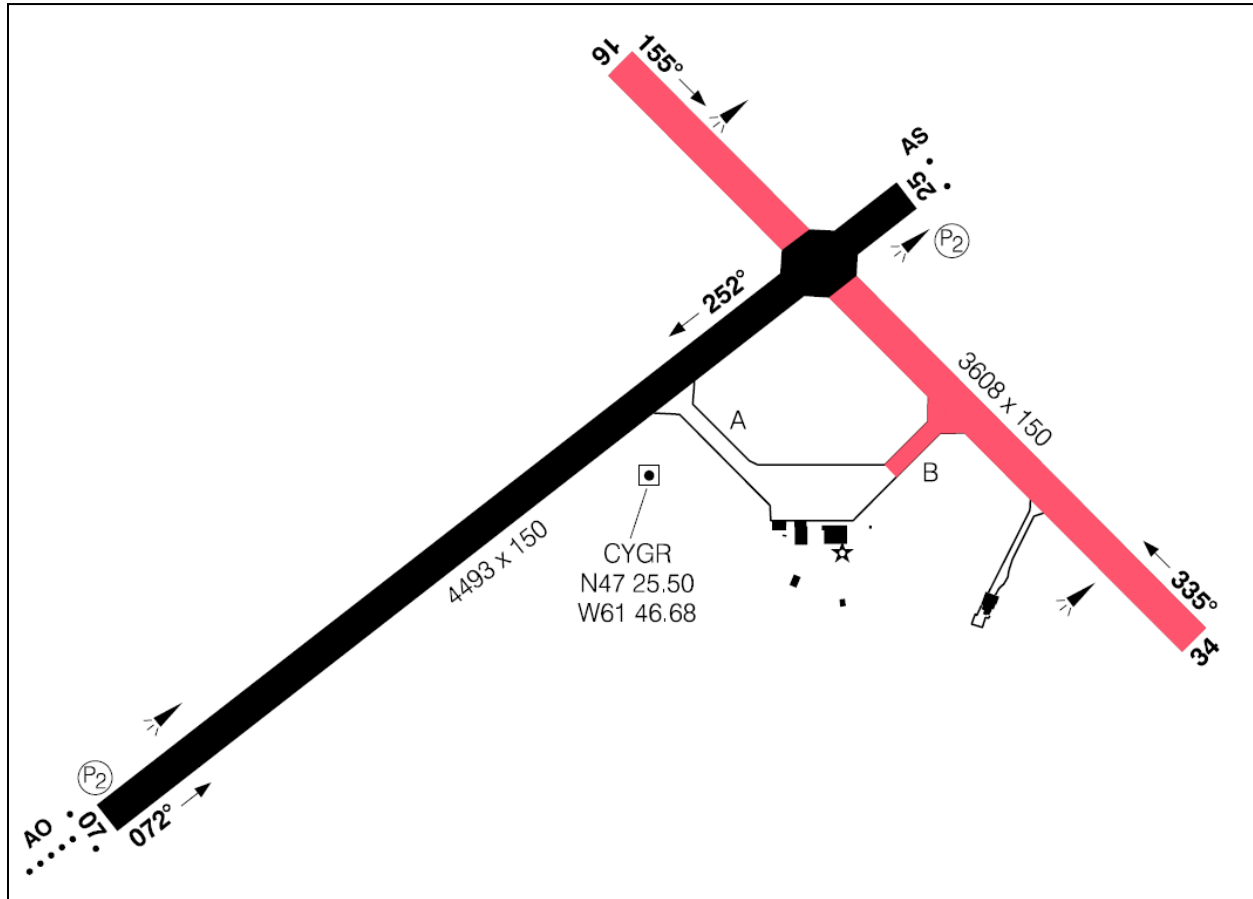
Temporary Depiction(s)

Figure 1. Overview of Phase 1A Construction Work

Closed Areas – Refer to NOTAMs

- Runway 16-34 closed
- Taxiway B closed

Restrictions and Operational Procedures – Refer to NOTAMs

- NIL

Instrument Procedures – Refer to NOTAMs

- NIL

Runway Physical Changes – Refer to NOTAMs


- NIL

Other Hazards

- Construction equipment (excavators, loaders, dump trucks, etc.) will be present during construction work hours at the indicated locations.
- Two lit "X" closed area markers will be installed at Threshold 16 and Threshold 34.
- TRV-7 barricades with obstruction lights will be placed every 3 m to delineate the boundary of the construction work area on paved surfaces and on Taxiway B.

Phase 1B (2300 UTC to 0900 UTC)**Planned Construction Period**

- From 21 to 25 September 2026, between 2300 UTC and 0900 UTC.

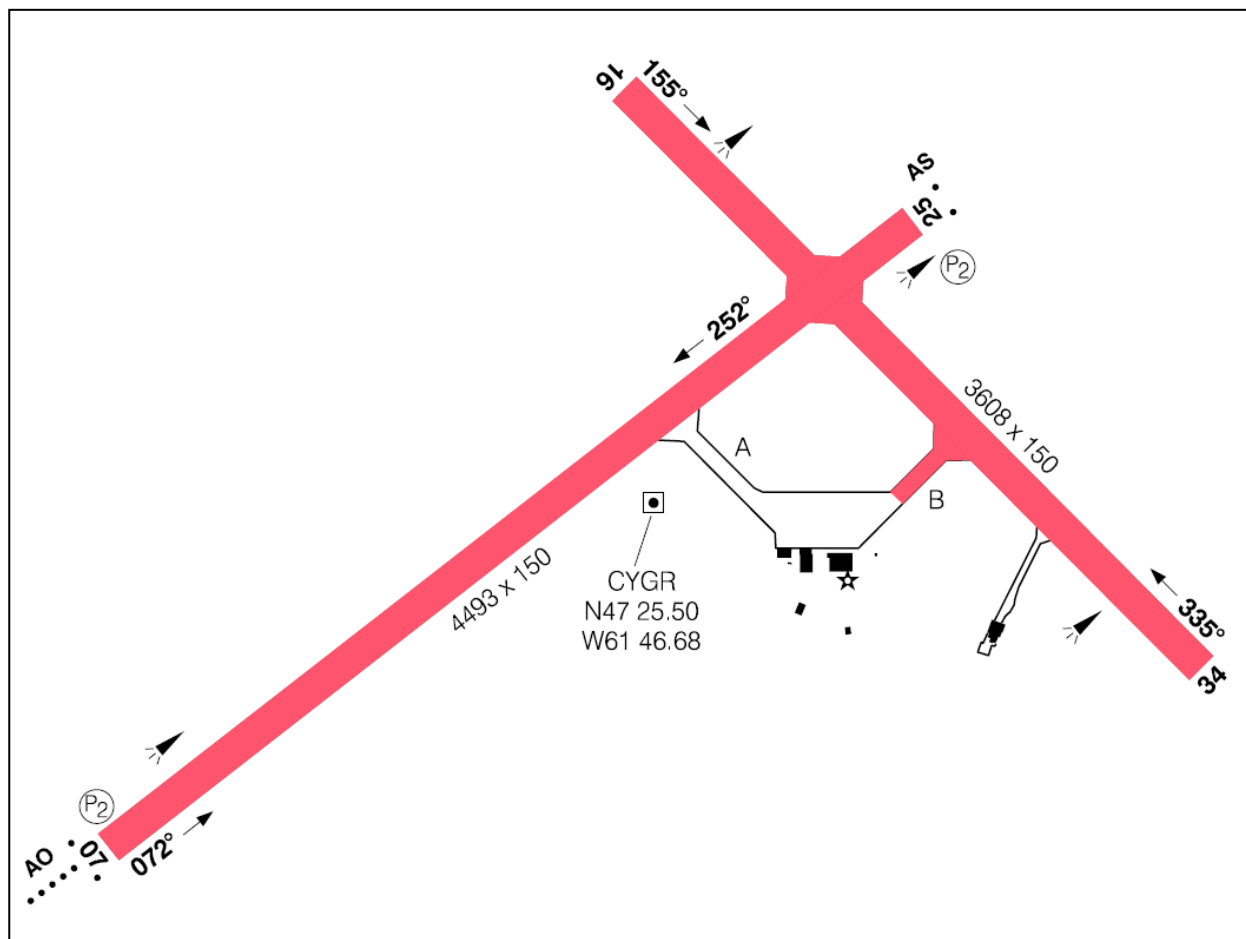Temporary Depiction(s)**Closed Areas – Refer to NOTAMs**

- Runway 16-34 closed
- Runway 07-25 closed between 2300 UTC and 0900 UTC. MEDEVAC flights may be accommodated with two (2) hours prior notice.
- Taxiway B closed

Phase 1B (0900 UTC to 2300 UTC)**Planned Construction Period**

- From 21 to 25 September 2026, between 0900 UTC and 2300 UTC

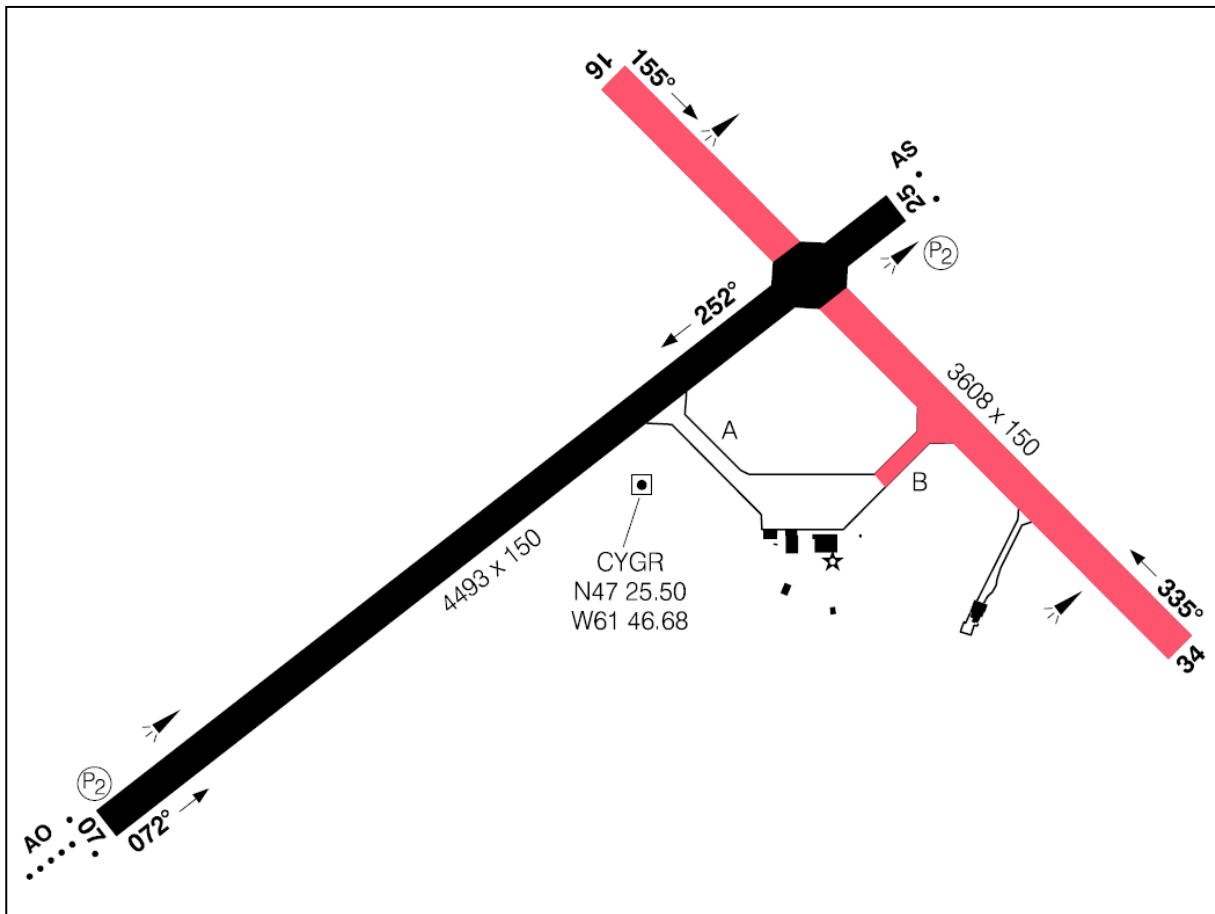
Temporary Depiction(s)

Figure 3. Overview of Phase 1B Construction Work

Restrictions and Operational Procedures – Refer to NOTAMs

- NIL

Instrument Procedures – Refer to NOTAMs

- NIL

Runway Physical Changes – Refer to NOTAMs

- NIL

Other Hazards

- Construction equipment (excavators, loaders, dump trucks, etc.) will be present during construction work hours at the indicated locations.



Figure 4. Lit "X" closed area markers

Further Information

For further information, please contact:

Gires Damen, Project Manager

Email: gires.damen@tc.gc.ca

Telephone: 581-459-2208
