

AIP CANADA SUPPLEMENT 19/21

TORONTO/LESTER B. PEARSON INTERNATIONAL AIRPORT, ONTARIO (CYYZ) CONSTRUCTION ACTIVITIES: SPRING 2021 THROUGH FALL 2021

Introduction

The scope and potential impacts of construction projects to be carried out at Toronto/Lester B. Pearson International Airport (CYYZ) from **mid-April 2021 to mid-October 2021** are outlined below.

Since all activities are subject to operational requirements and construction schedules, actual dates and times of construction activities will be promulgated through briefing documents and NOTAMs.

CYYZ Runway and Taxiway Identification

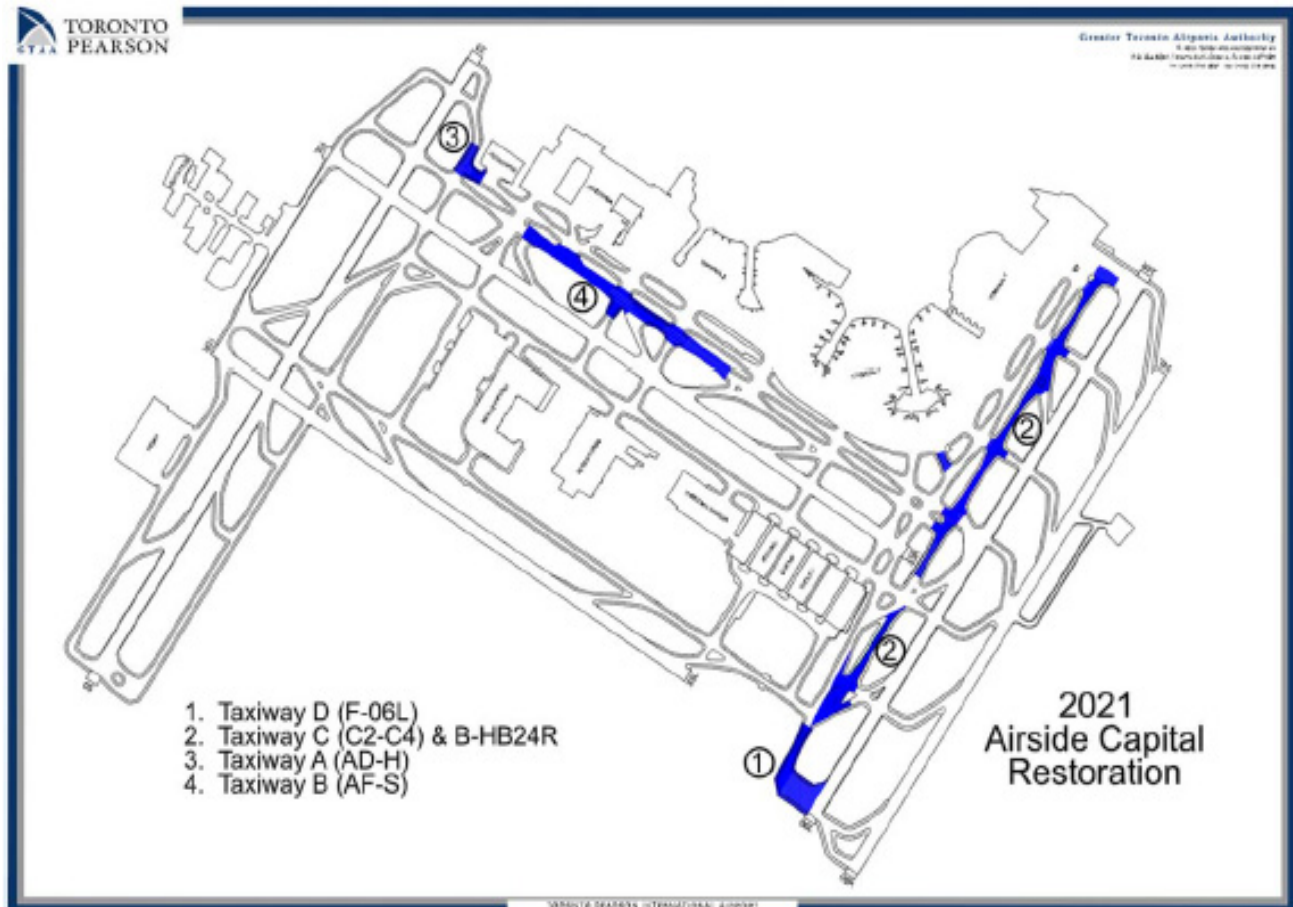


Figure 1: CYYZ Runway and Taxiway Identification Diagram

Phase 1: Construction for Taxiway DELTA (Area 1)

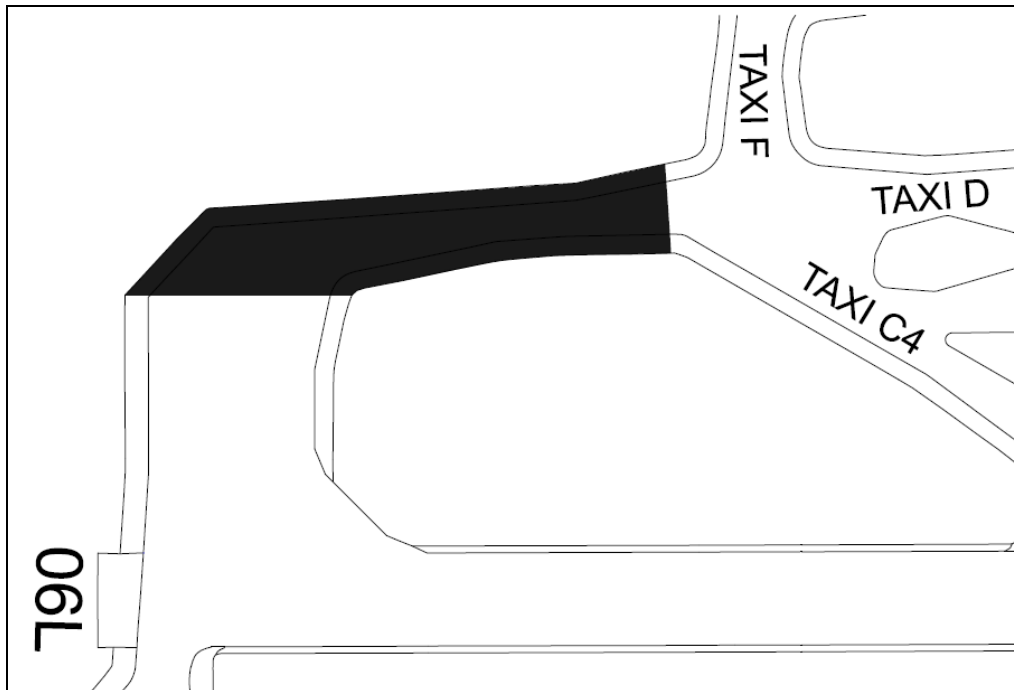



Figure 2: Taxiway DELTA Phase 1 Construction (Area 1)

Dates: Mid-April 2021 to late June 2021 (approx. 8 weeks)

Scope: Taxiway surface rehabilitation and lighting upgrade

Impacts:

- Runway 06L/24R; **closed**, available as taxiway.
- Taxiway D **closed** between Threshold 06L and Taxiway F

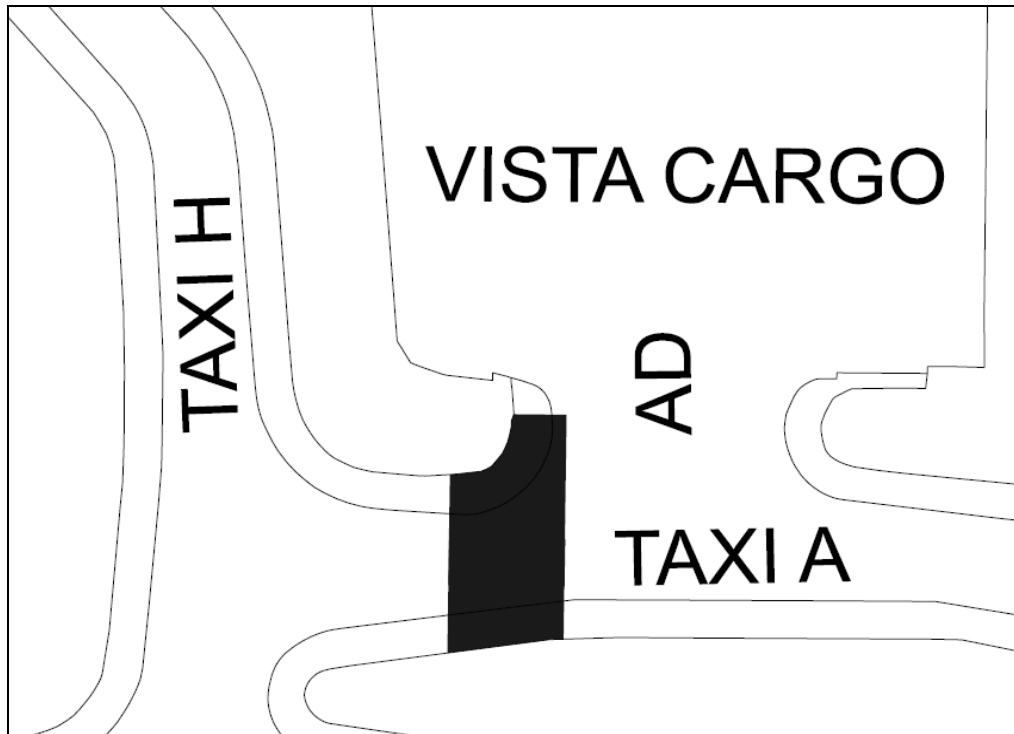Phase 1(A): Construction for Taxiway ALPHA (Area 3)**Figure 3: Taxiway ALPHA Phase 1(A) Construction (Area 3)**

Dates: Early May 2021 to mid-May 2021 (approx. 6 days)

Scope: Taxiway surface and base rehabilitation

Impacts:

- Taxiway A **closed** between Taxiway H and Taxiway AD
- Taxiway AD available with 30 min PPR
- Push-back from Vista Cargo must disconnect south of Taxiway AE

Phase 2(A): Construction for Taxiway ALPHA (Area 3)

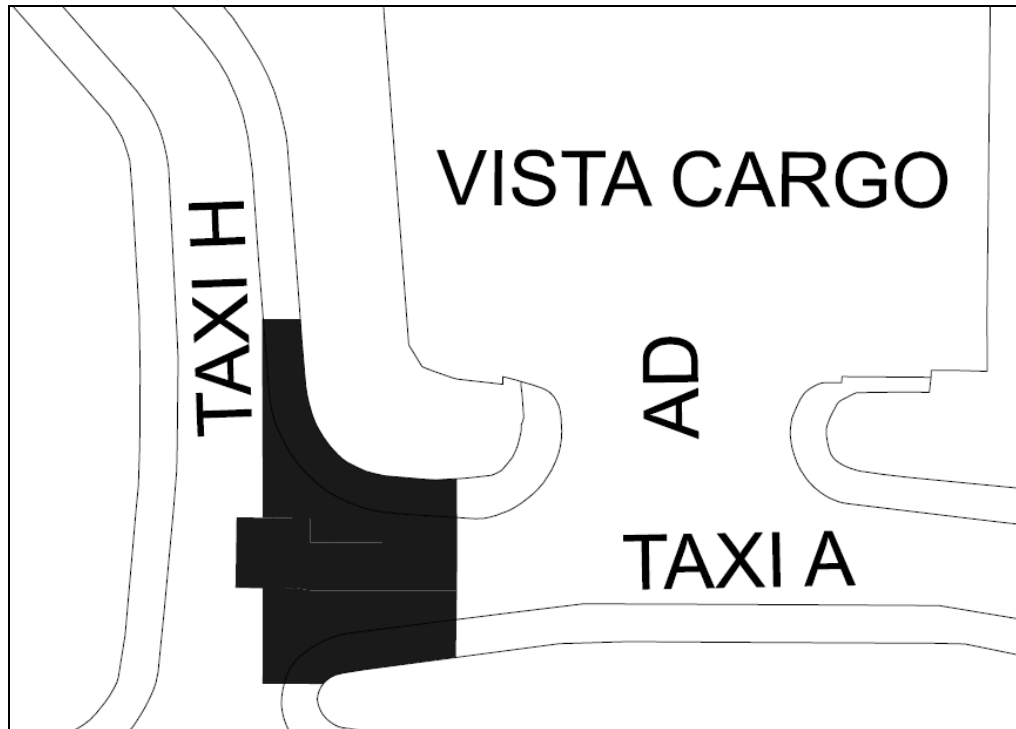



Figure 4: Taxiway ALPHA Phase 2(A) Construction (Area 3)

Dates: Late May 2021 to mid-June 2021 (approx. 21 days)

Scope: Taxiway surface and base rehabilitation

Impacts:

- Taxiway H **closed** between Taxiway B and Runway 05/23
- Taxiway A **closed** between Taxiway H and Taxiway AD
- Taxiway Q **closed**

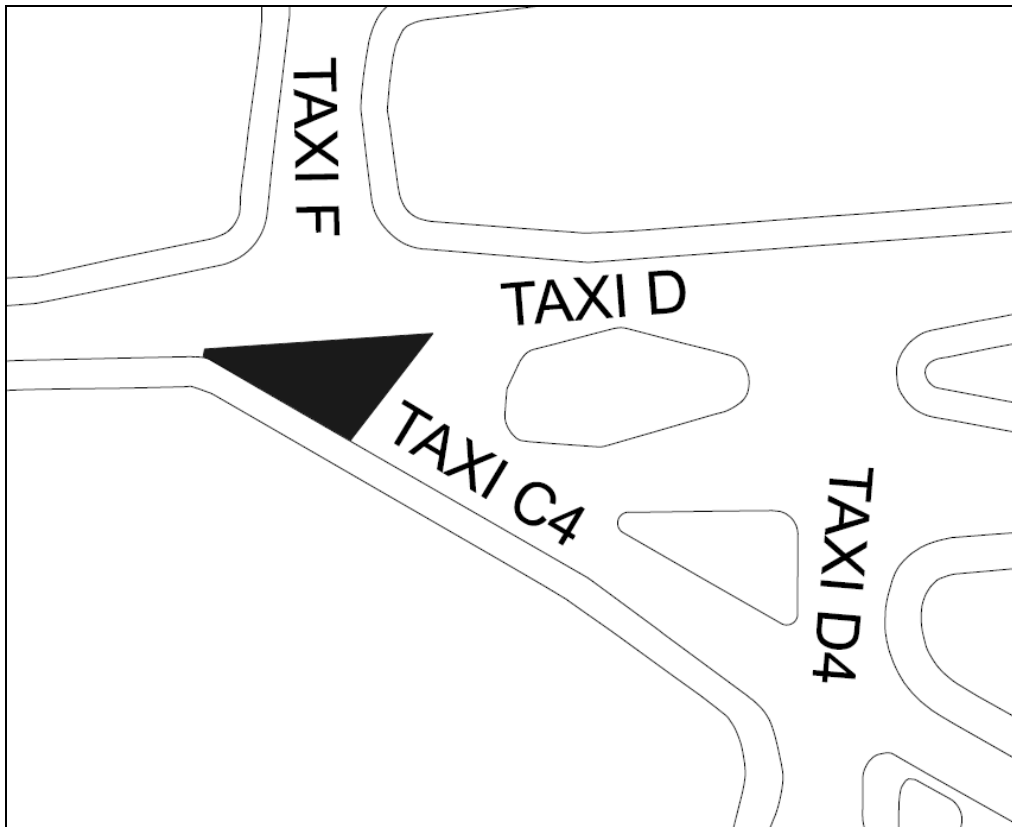Phase 1: Construction for Taxiway CHARLIE (Area 2)**Figure 5: Taxiway CHARLIE Phase 1 Construction (Area 2)**

Dates: Early June 2021 to late June 2021 (approx. 18 days)

Scope: Taxiway surface and base rehabilitation

Impacts:

- Runway 06L/24R; **Not authorized for landing or take-off**, available as taxiway.
- Taxiway D **closed** between Threshold 06L and Taxiway D4
- Taxiway C4 **closed** between Taxiway D4 and Taxiway D
- Taxiway C **closed** between Taxiway C4 and Taxiway D4
- Taxiway F **closed** between Taxiway V and Taxiway D

Phase 2: Construction for Taxiway CHARLIE (Area 2)**Figure 6: Taxiway CHARLIE Phase 2 Construction (Area 2)**

Dates: Late June 2021 to late July 2021 (approx. 24 days)

Scope: Taxiway surface and base rehabilitation

Impacts:

- Runway 06L/24R; **Not authorized for landing or take-off**, available as taxiway.
- Taxiway D **closed** between Taxiway F and Taxiway E
- Taxiway C4 **closed**
- Taxiway D4 **closed** between Runway 06L and D
- Taxiway C **closed** between Taxiway E and Taxiway C4
- Taxiway C2 **closed** between Taxiway E and Taxiway D

Phase 3: Construction for Taxiway CHARLIE (Area 2)

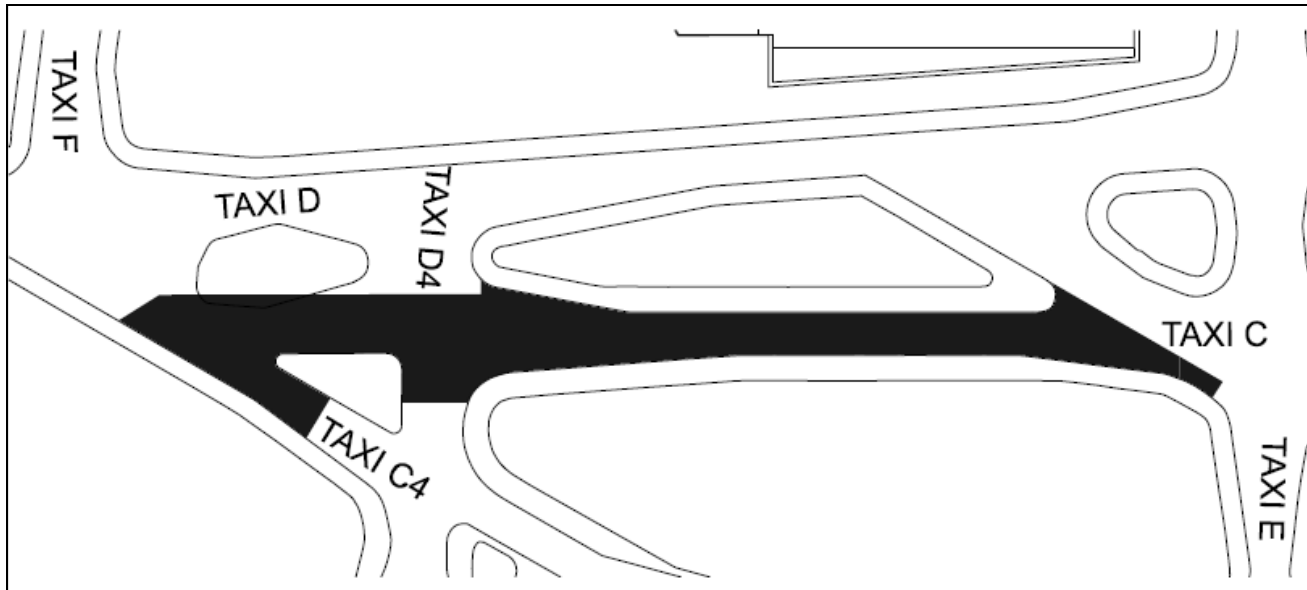



Figure 7: Taxiway CHARLIE Phase 3 Construction (Area 2)

Dates: Mid-July 2021 to mid-August 2021 (approx. 24 days)

Scope: Taxiway surface and base rehabilitation

Impacts:

- Runway 06L/24R; **Not authorized for landing or take-off**, available as taxiway.
- Taxiway C **closed** between Taxiway C4 and E
- Taxiway C4 **closed**
- Taxiway D4 **closed** between Runway 06L and D
- Taxiway C2 **closed** between Taxiway E and Taxiway D

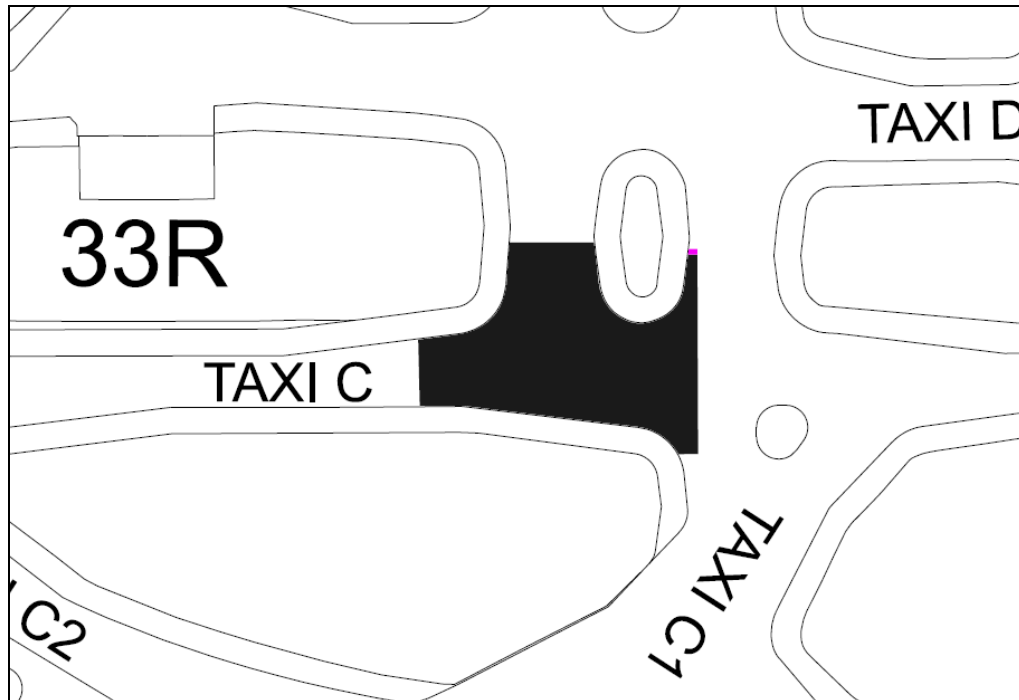Phase 4: Construction for Taxiway CHARLIE (Area 2)**Figure 8: Taxiway CHARLIE Phase 4 Construction (Area 2)**

Dates: Mid-August 2021 to early September 2021 (approx. 12 days)

Scope: Taxiway surface and base rehabilitation

Impacts:

- Runway 06L/24R; **Not authorized for landing or take-off**, available as taxiway.
- Runway 15L/33R restricted to **Non-Instrument**
- Taxiway C **closed** between Taxiway C2 and Taxiways D3
- Taxiway C1 **closed** between Runway 06L and Taxiway C
- Taxiway A **closed** between Taxiway D and Taxiway C
- Taxiway B **closed** between Taxiway D and Taxiway C

Phase 5: Construction for Taxiway CHARLIE (Area 2)

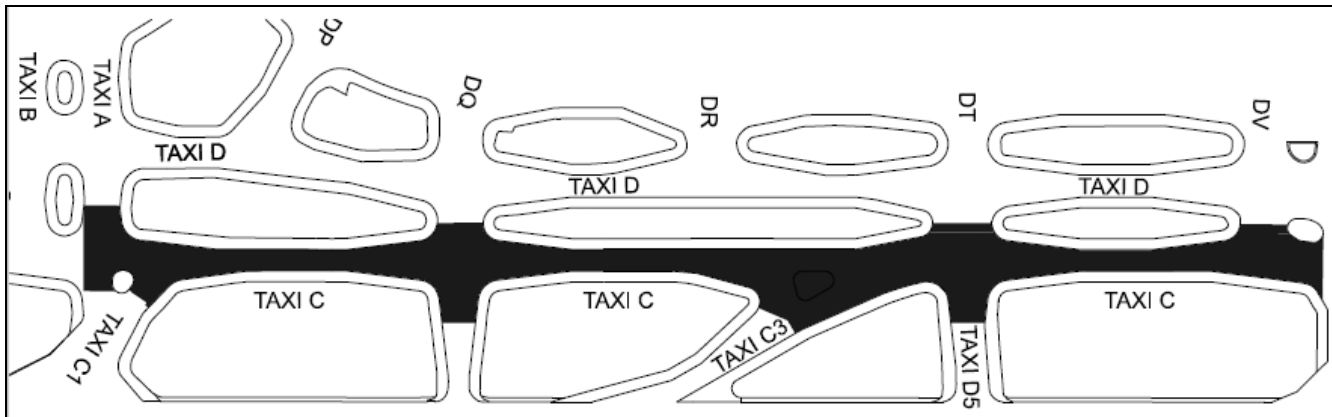



Figure 9: Taxiway CHARLIE Phase 5 Construction (Area 2)

Dates: Mid-August 2021 to mid-October 2021 (approx. 48 days)

Scope: Taxiway surface and base rehabilitation

Impacts:

- Runway 06L/24R; **not authorized for landing or take-off**, available as taxiway.
- Taxiway C **closed** between Taxiway B and HB24R
- Taxiway C1, C3, D3, D5 **closed** between Runway 06L and Taxiway C
- Taxiway A **closed** between Taxiway D and Taxiway C
- Holding Bay 24R West Lane **closed**
- Phase 5A, 5B, 5C nightwork only Taxiway D restricted to Code C and smaller between Taxiway DP and Taxiway HB24R

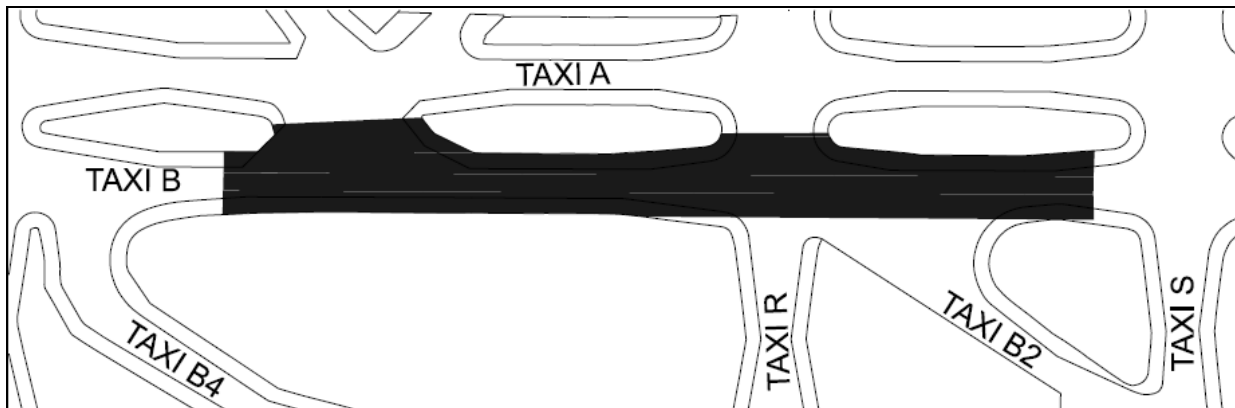Phase 4: Construction for Taxiway BRAVO (Area 4)**Figure 10: Taxiway BRAVO Phase 1 Construction (Area 4)**

Dates: Mid-August 2021 to late September 2021 (approx. 35 days)

Scope: Taxiway surface and base rehabilitation

Impacts:

- Taxiway B **closed** between Taxiway S and Taxiway B4
- Taxiways B2 and B4 **closed**
- Taxiway R **closed** between Runway 15L/33R and Taxiway A
- No turning from Taxiway B4 to Taxiway B southbound
- Taxiway AT **restricted** to Code C
- Taxiway AF **restricted** to Code C unless aircraft are under tow
- Runway 15L/33R **closed** nightly for Phase 1C

Phase 2: Construction for Taxiway BRAVO (Area 4)

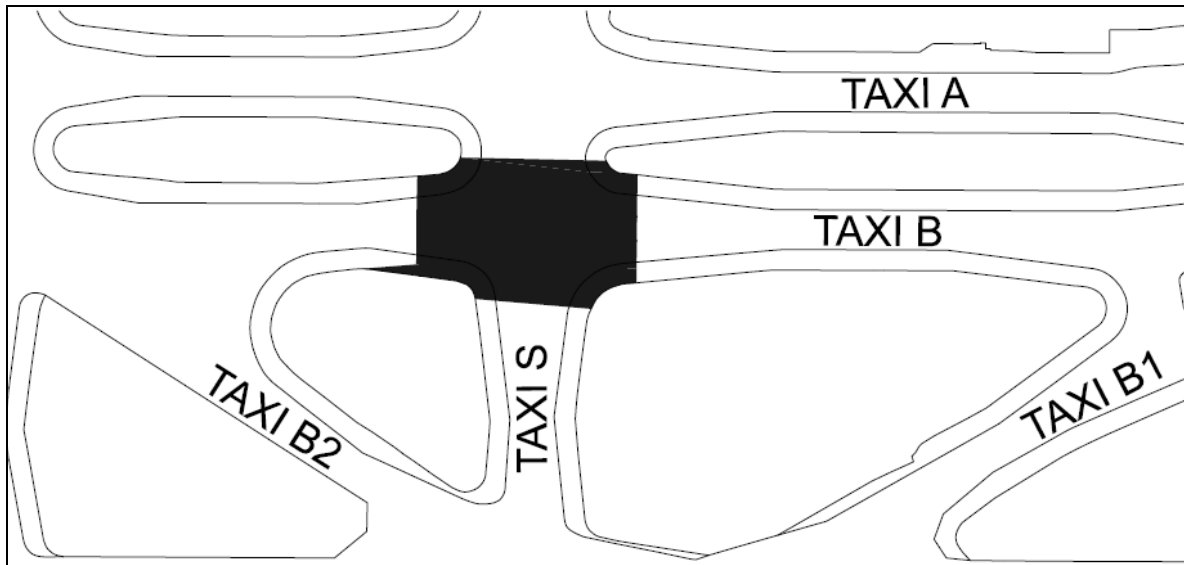


Figure 11: Taxiway BRAVO Phase 2 Construction (Area 4)

Dates: Late August 2021 to early September 2021 (approx. 6 days)

Scope: Taxiway surface rehabilitation

Impacts:

- Taxiway B **closed** between Taxiway B1 and Taxiway B2
- Taxiway B **closed** between Taxiway R and Taxiway N
- Taxiway S **closed** between Runway 15L/33R and Taxiway A
- Taxiway B4 **closed**
- No turning from Taxiway B2 to Taxiway B
- No turning from Taxiway R to Taxiway B
- Taxiway AJ **restricted** to Code C
- Taxiway A **restricted** nightly to Code C between Taxiway AT and Taxiway AK for Phase 2A

Further Information

For further information, please contact:

Greater Toronto Airports Authority
PO Box 6031
3111 Convair Drive
Toronto, ON L5P 1B2
Attn: Andrew Payter, Aviation Services

Tel.: 416-776-3441
E-mail: andrew.payter@gtaa.com



Stephanie Castonguay
Director, Aeronautical Information Management and Flight Operations
